WORK PROGRAMME/PLAN FOR PROPOSED CONSTRUCTION OF PUBLIC HEALTH AND TOXICOLOGICAL RESEARCH CENTRE, UNIVERSITY OF PORT HARCOURT CHOBA.
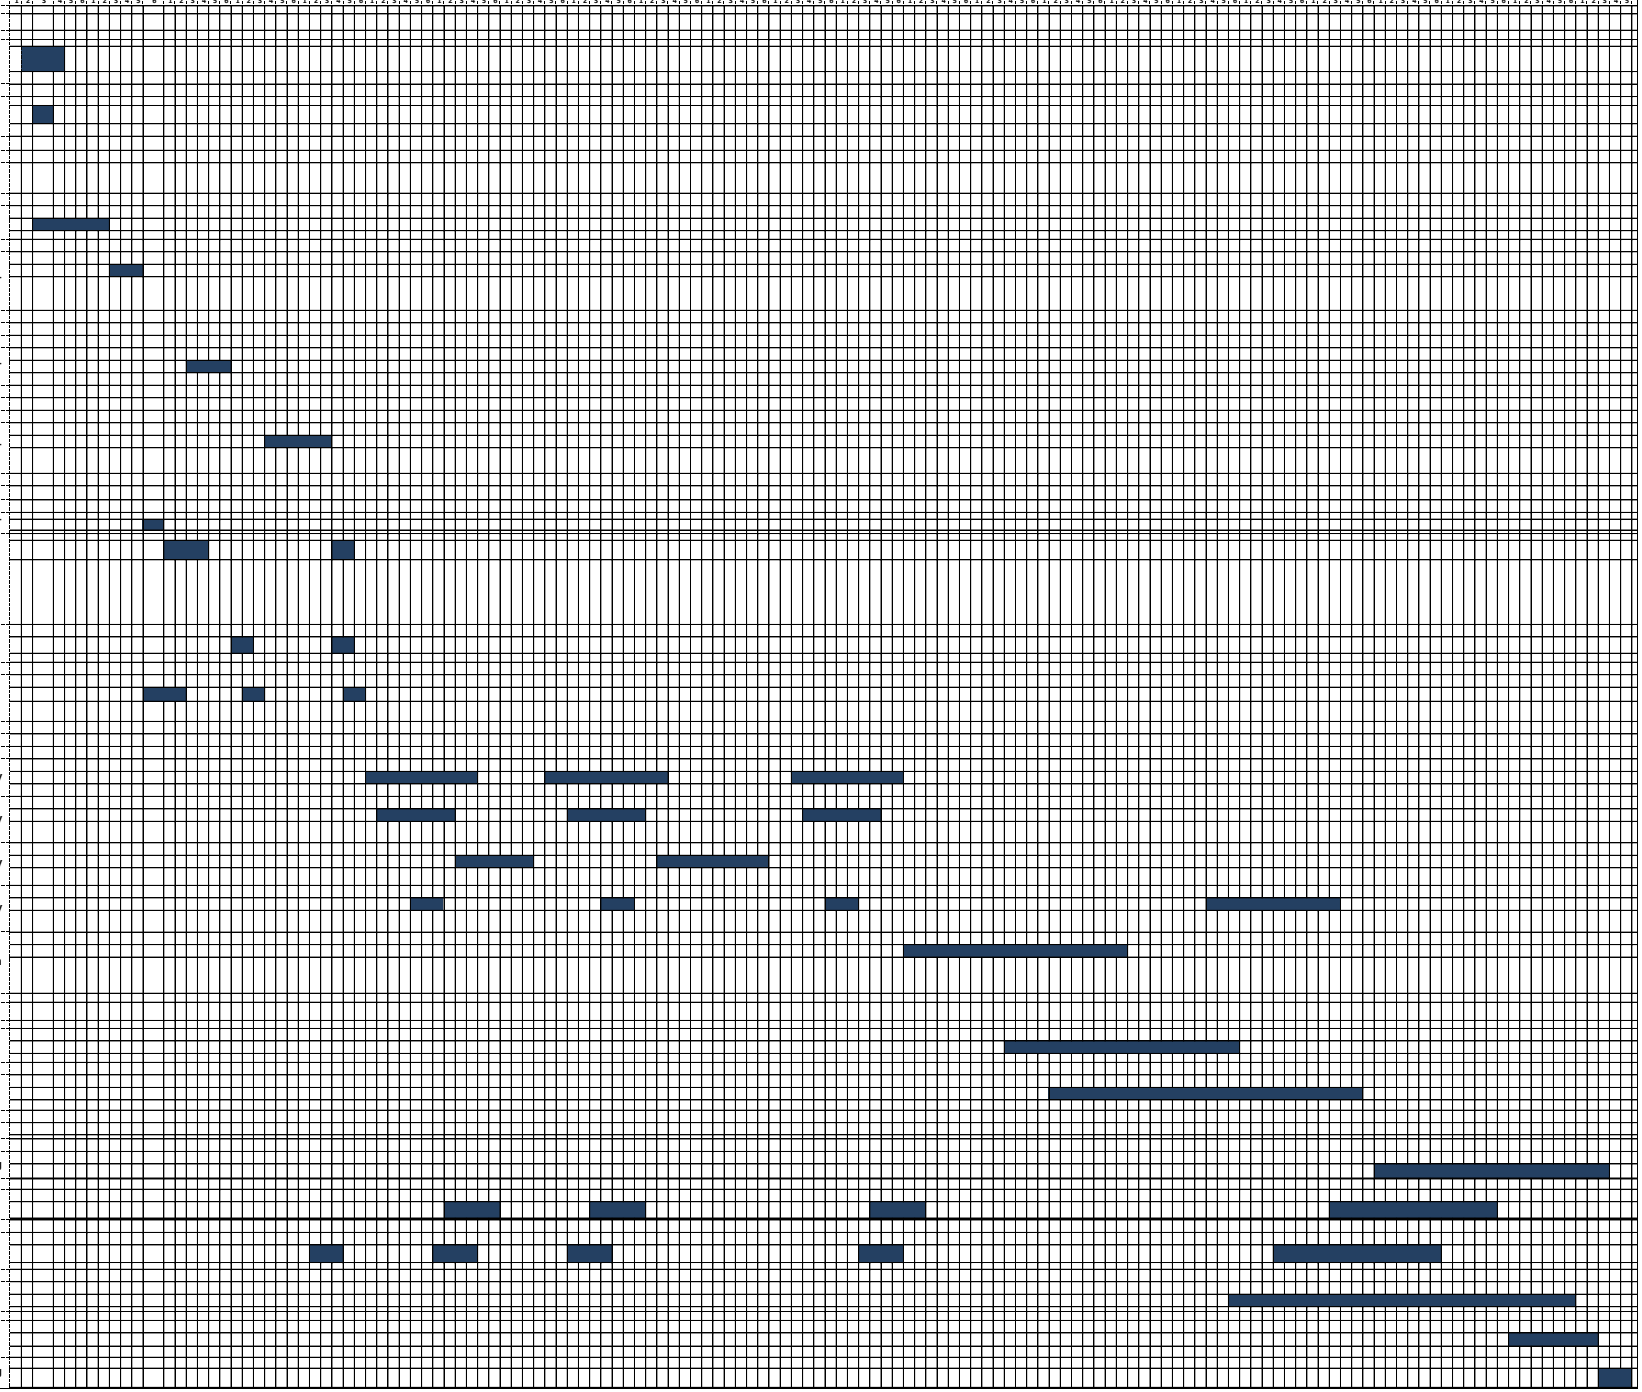
S/N	WORK DESCRIPTION	DURATION (DAYS)	START DATE	END DATE
	PRELIMINARIES			
1	Mobilization and Site preparation	3	1-Mar	3-Mar
2	Setting Out	1	2-Mar	2-Mar
	SUBSTRUCTURE			
	EXCAVATION AND EARTHWORKS			
3	Excavation: Trench and Column Base	6	2-Mar	8-Mar
4	Trench Preparation: Level and compacting, Earth work support and Antitermite treatment	3	9-Mar	11-Mar
	BLOCK WORKS			
5	225mm and 150mm Block laying in foundation	4	16-Mar	19-Mar
	FILLING			
6	Filling works: Back filling, Laterite filling, Hardcore and sharp sand filling.	6	24-Mar	30-Mar
	CONCRETE WORKS			
7	Blinding	1	12-Mar	12-Mar
8	Reinforcement:12mm,16mm diameter, 8mm for stirrups and BRC Mesh (for Column bases, columns and Ground floor slab)	6	14-Mar	1-Apr
9	Formwork: Columns and Slab	4	21-Mar	1-Apr
10	Mass concrete (foundation base, column and ground floor slab)	7	12-Mar	2-Apr
	SUPERSTRUCTURE			
11	Frames: Columns and Beams	30	4-Apr	28-May
12	225mm and 150mm Block laying: Ground, First and second floors	21	5-Apr	26-May
13	Suspended Slab and Staircase: First and Second floors	20	13-Apr	14-May
14	DOORS AND WINDOWS WORKS: Lintels, Doors and Windows	21	8-Apr	24-May
15	Roofing: Roof Beam, Fascia, Structural members and roofing sheets	20	30-May	21-Jun
	FINISHINGS			
16	CEILING: POP and Suspended Ceiling	21	9-Jun	2-Jul
17	PLASTERING: External and Internal wall plastering	28	14-Jun	15-Jul
18	TILING	20	18-Jun	11-Jul
19	SCREEDING AND PAINTING	21	18-Jul	10-Aug
20	ELECTRICAL INSTALLATION	30	12-Apr	29-Jul
21	MECHANICAL AND PLUMBING WORKS	30	29-Mar	23-Jul
22	EXTERNAL WORKS	31	2-Jul	6-Aug
23	SITE CLEAN UP AND DEMOBILIZATION	8	1-Aug	9-Aug
24	HAND OVER	3	10-Aug	12-Aug
